SIVPL/PEB: Ref: No:/1003 Date: 09/10/2026

QUOTATION

To
self,
Kind Attn: Mohamed Sameer,
Phone: +918148771210
Email: sameerkaleemi10@gmail.com

Sub: Supply & Erection of Pre-Engineered Building (PEB) for your MULTI SPAN 3 BUILDING Project at Chennai - reg

Dear Sir,

With reference to your inquiry, and subsequent discussion we had had with you, please find enclosed here with our proposal for your kind perusal.

We believe that our Indexed Proposal / Offer will facilitate easy reference.

In case you do require any further clarifications, please feel free to revert to the undersigned with your queries.

Thanking you and assuring you of our best services at all times, we remain,

Very truly yours,
For Senela International Ventures Pvt. Ltd.



R. Elangovan
9942466663

SIVPL/PEB: Ref: No:/1003 Date: 09/10/2026

PROPOSAL INDEX

Section	DESCRIPTION	PAGE
1	Building Description	03
2	Standard Supplied Material	04
3	Material Specification	05
4	Steel Work Finish	06
5	Completion Period	06
6	Proposal validity	06
7	Prices	07
8	Assumptions & Deviations	08
9	Force Majeure Clause	08

SIVPL/PEB: Ref: No:/1003 Date: 09/10/2026

Section 1. BUILDING DESCRIPTION

BUILDING DESCRIPTION		
S.No.	Parameter	Details
1	Building type	Multi Span 3
2	Type of Column	R.C.C
3	Type of End Frame	Light Frame
4	Length in mtr/ft (o/o of steel)	NA
5	Width in mtr/ft (o/o of steel)	NA
6	Left eave height	NA
7	Right eave height	NA
8	Ridge line distance	NA
9	Roof slope (ratio,deg)	NA
10	Left end wall bay spacing	NA
11	Right end wall bay spacing	NA
12	Side wall bay spacing	NA
13	Wall bracing type	Rod
14	Roof bracing type	Rod
15	Roof sheeting	CCGI, 2mm, RAL green
16	Wall sheeting	CCGI
17	Brick wall Height	NA

DESIGN & LOADING		
Sr no.	Parameter	Details
1	Design code	AISC code
2	Dead Load in kN/m2	0.1
3	Live Load in kN/m2	0.57
4	Collateral load kN/m2	0
5	Max wind speed in m/s	44
6	Max rainfall intensity in mm/hr.	150
7	Exposure category	B
8	Seismic zone co-efficient (III)	0.24
9	Maximum temperate variation	20
Sr no.	Parameter	Details
1	Frames Vertical deflection	Span/150
2	Frames Horizontal deflection	Height/100
3	Purlins	Span/150
4	Girts	Span/120
5	Crane beams	Span/600
6	Mezzanine beams	Span/240

SIVPL/PEB: Ref: No:/1003 Date: 09/10/2026

7	Misc	NA

Sr no.	Assumption/Remark	Details
1	Hot rolled sections grade (Mpa)	250
2	Cold form sections grade (Mpa)	350
3	Primary sections grade (Mpa)	350
4	Building design condition	Enclosed
5	Minimum web thickness in mm	4
6	Minimum flange thickness in mm	5
7	Minimum flange width in mm	125
8	Minimum web depth in mm	250
9	Minimum cold form thickness in mm	1.5
10	Sheeting profile width & length in m	1.22 & 7.65
11	Connection bolts grade	High strength bolts (ASTM A325 or equivalent)

Crane 1		
1	Crane Capacity in kN	NA
2	Crane beam top height	NA
3	Crane span	NA
4	Crane starting point	NA
5	Crane running length	NA
6	Crane class	NA
7	Crane Type	NA
8	Type of Girder	NA
9	Bridge Weight in MT	NA
10	Hoist/Trolley Weight in MT	NA
11	Number of Wheels	NA
12	Wheel Load in MT	NA
13	Wheel Base in mm	NA

EXCLUSIONS:

1. Roof/wall extracts fans & other exhaust systems
2. All doors/windows, rolling shutter
3. Masonry work & supervision.
4. Miscellaneous steel except as specified herein.
5. Crane Girder and Accessories

Section 2. Standard Supplied Items:

The materials supplied by Senela are as per the Standards applicable to Senela Buildings.

SIVPL/PEB: Ref: No:/1003 Date: 09/10/2026

1. Anchor Bolts.
2. Flashing and Trims
3. Closure Strips
4. Sealing Tape
5. Rod Bracing
6. Connection Bolt
7. Sheeting Fasteners

Section 3. Material Specification

A. ANCHOR BOLT

The steel column strut of Pre-Engineered Building and RCC interface shall be designed as a fixed/pinned base with a minimum of 20 mm Dia anchor bolt according to the design calculation.

B. ROOFING SHEET: GALVALUME

Providing and Fixing of single Skin Senela Profile, Overall Width of 1060 mm and covered width of 1000mm, with six Crests (29mm crest height, width of 25 mm at the top of the crest and 74 mm at the base of the crest), spaced at 200 mm - crest centre to centre, and with two stiffening ribs (20mm) at the centre of each valley of the sheet, with two anti-capillary grooves (5 mm) on either side of each crest making the Trapezoidal Profile the best in the Industry in terms of appearance, strength and cost effectiveness.

C. CLADDING: COLOR COATED GALVALUME

Providing and Fixing of single Skin Senela Profile, Overall Width of 1060 mm and covered width of 1000mm, with six Crests (29mm crest height, width of 25 mm at the top of the crest and 74 mm at the base of the crest), spaced at 200 mm - crest centre to centre, and with two stiffening ribs (20mm) at the centre of each valley of the sheet, with two anti-capillary grooves (5 mm) on either side of each crest making the Trapezoidal Profile the best in the Industry in terms of appearance, strength and cost effectiveness.

D. SHEETING FASTENERS

The sheets will be fastened with No.14-10 x 20mm (or as per design) galvanized hex-self tapping metal screws of approved make and quality including EPDM / Neoprene washer on each crest of sheets for connecting with purlins (or as per design).

SIVPL/PEB: Ref: No:/1003 Date: 09/10/2026

E. FLASHING AND TRIMS:

Suitable flashing shall be provided at the eaves in PPGI Sheets. Material used for manufacture of Flashing shall be same as that of wall cladding. Flashing shall be provided at the junction/termination edges of sheeting, vertical corners, barge-roof to wall cladding etc., to ensure neat finish and trims, flashing be matching to wall cladding.

F. SEALER:

Sealer should be applied as per requirement at side laps and end laps of roof panels and around self flashing windows. Sealer shall be 6 mm wide x 5 mm thick, asbestos fiber filled pressure sensitive Butyl tapes. The sealer shall be non-asphalted, non-shrinking, non-drying and non-toxic and shall have superior adhesion to metals, plastics and painted surfaces at temperatures from –51 degree Celsius to +104 degrees Celsius.

Section 4. Steel Work Finish: (Primary & Secondary Steel):

Primary steel shall be cleaned to specification St2. One shop primer coat of Red Oxide primer shall be applied with an average dry film Thickness of 25 microns on all red steel. Shop primer provides protection for elements while in transit and construction and is not intended to be for permanent protection. The final paint ENAMEL will be applied at site.

Section 5. Completion Period:

3.1 Completion period is 08 -10 Weeks from the date of receipt and acceptance of the following:

I) Signed Contract (Any change must be noted and initialed by both parties).

Ii) As per payment terms.

Iii) Final change order.

iv) Signed final "approved as noted" Approval Drawings.

3.2 Please allow a minimum of 10 Days for Approval Drawings to be submitted. Approval drawings must be returned to our Office within 7 Days of receipt by customer. Any delay in the return of the approval drawings back to Senela may result in change in delivery commitment.

Section 6. Proposal Validity:

This proposal is valid for 15 days from the above noted date. Any extension of validity by Senela International Ventures Pvt Ltd must be in writing.

SIVPL/PEB: Ref: No:/1003 Date: 09/10/2026

Changes/Revisions:

Any change and /or revision to the above stated scope of supply may lead to a variation in the price and the delivery period. A change must not hold payment for work completed in the original contract.

Section 7. PRICES :Pre-Engineered Steel Building

PRE-ENGINEERED STEEL BUILDING – MULTI SPAN 3				
SL.NO	PARTICULAR	AREA	RATE/SQFT	AMOUNT(RS)
1	PRE-ENGINEERED STEEL BUILDING – MULTI SPAN 3 – 54 X 54 ft ☑ Structural Design ☑ Structural Detailing ☑ Structural Fabrication ☑ Supply & Installation of structure ☑ Supply & Fixing of Roofing & cladding	2,916 SQ. FT	₹200	₹5,83,200/-

OPTIONAL

i) Civil Works: RCC foundations, footings, flooring, and civil masonry works are excluded from the above scope and will be quoted separately, if required to be included in our scope.

ii) Roof Ventilator will be charged at Rs.7500/- per piece.

iii) Doors & Windows will be charged at actual.

iv) Transport will be extra at actual.

1. Terms & Conditions:

GST 18% excluding; Taxes are subjected to change as levied by the Government. If there is any change in GST Tax, Excise tariff or statutory levels imposed by the government at the time of shipment, such additional charges to be borne by the Buyer.

2. Payment Terms:

- 10% Advance along with Work order / Signed contract.
- 40% At the stage of approval of drawings or design report.
- 25% Against PEB Materials in-ward at site (Before Erection).
- 20% Against completion of Structural Erection (Before Sheeting).
- 05% Against completion of Sheet fixing.

SIVPL/PEB: Ref: No:/1003 Date: 09/10/2026

3. Bank Details

Beneficiary Name	: Senela International Ventures Pvt Ltd
Bank Name	: ICICI Bank
Account Number	: 603705020036
IFSC Code	: ICIC0006037
Branch	: ICICI Bank Limited, 236, Velachery Main Road, Selaiyur, Chennai – 600073

Section 8. Assumption, Deviations & Exclusions:

1. Items and codes which are not mentioned in this proposal are not in Senela International Scope of supply.

2. It is the customer's responsibility to verify that the specified loads are adequate for the building use.

3. Electricity 3 phase supply and water to be provided free of cost at site during the erection of structures.

4. Force Majeure Clause will be applicable.

5. Building measurement should be taken O/O of metal sheet line only.

Section 9. Force Majeure Clause:

Standard Force Majeure Clause will be applicable.

SELLER shall not be liable for any loss or damage to BUYER for delay in delivery or non - Delivery, but not limited to war riots, civil commotion, insurrections, revolution, civil war, regulations, orders or acts of any authority directly or indirectly interfering more burdensome the production or delivery of the products, floods fires weather conditions, factory Pg shutdown or alterations, embargoes, delays in or shortage of transportation or inability to obtain labor power failure and any other circumstance or event Beyond The Control Of The Seller.

SIVPL/PEB: Ref: No:/1003 Date: 09/10/2026

Governing Law:

This Agreement shall be construed and endorsed in accordance with and under the laws of the Republic of India. Both parties agree that the Indian Courts shall be the competent ones to hear any dispute arising out of or in connection with this Agreement. Despite the foregoing or any other future understanding or Agreement wherever it is provided for SELLER shall also have the right to take legal action and proceedings before the courts of the BUYER's place of business or any other jurisdiction where BUYER may have property or assets.


We thank you for your enquiry and look forward to receiving your valuable purchase order.

For SENELA INTERNATIONAL VENTURES PVT LTD




Authorized Signatory

REFERENCE IMAGES

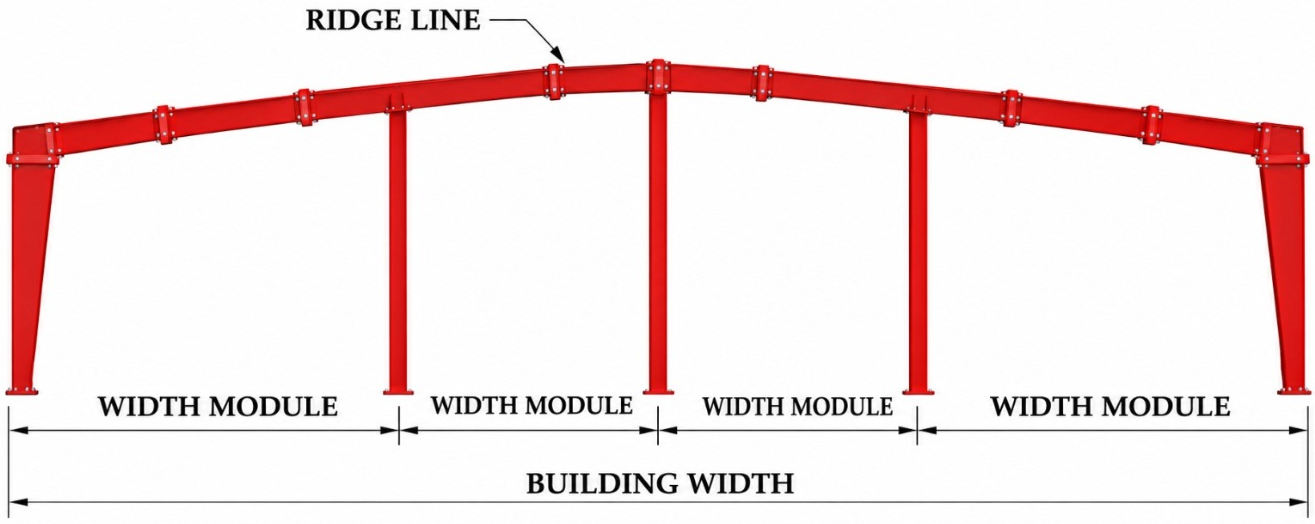

Type of building – Multi Span 3

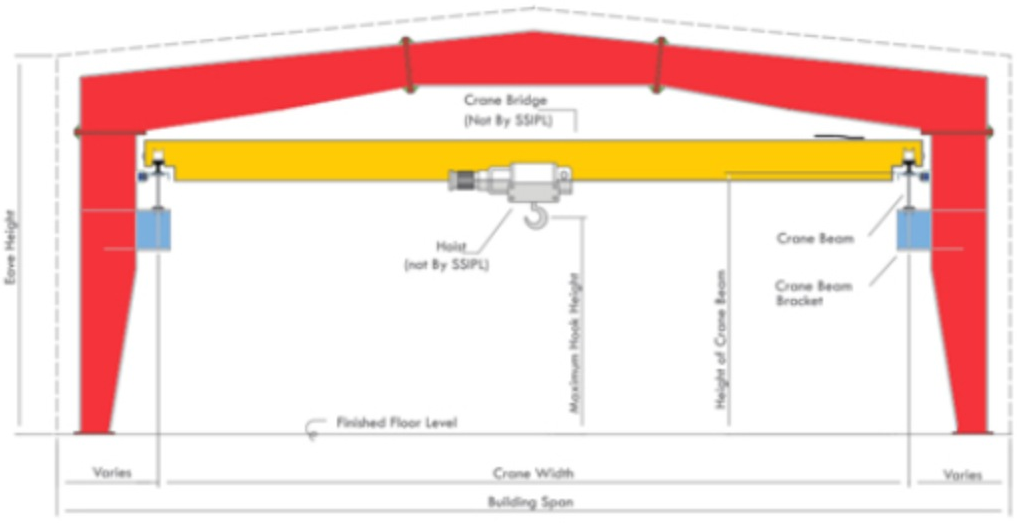

Crane and hoist
